ID	Task Name	Duration	Start	Finish	Predecessors
1	Proposal and budget	1 wk	Fri 01/01/10	Thu 07/01/10	
2	Board approval	1 wk	Fri 08/01/10	Thu 14/01/10	1
3	Detailed drawings	2 wks	Fri 15/01/10	Thu 28/01/10	2
4	Building permits	2 wks	Fri 29/01/10	Thu 11/02/10	3
5	Construct building	6 wks	Fri 12/02/10	Thu 25/03/10	4
6	Recruit staff	9 wks	Fri 15/01/10	Thu 18/03/10	2
7	Select furniture supplier	2 wks	Fri 15/01/10	Thu 28/01/10	2
8	Order furniture	6 wks	Fri 19/03/10	Thu 29/04/10	6,7
9	Order computers	4 wks	Fri 15/01/10	Thu 11/02/10	2
10	Complete interiors	2 wks	Fri 26/03/10	Thu 08/04/10	5
11	Parking lot	1 wk	Fri 26/03/10	Thu 01/04/10	5
12	Building inspection	1 wk	Fri 09/04/10	Thu 15/04/10	10
13	Install furniture	1 wk	Fri 30/04/10	Thu 06/05/10	8,12
14	Install computers	1 wk	Fri 07/05/10	Thu 13/05/10	9,13
15	Building occupied	0 days	Thu 13/05/10	Thu 13/05/10	11,14

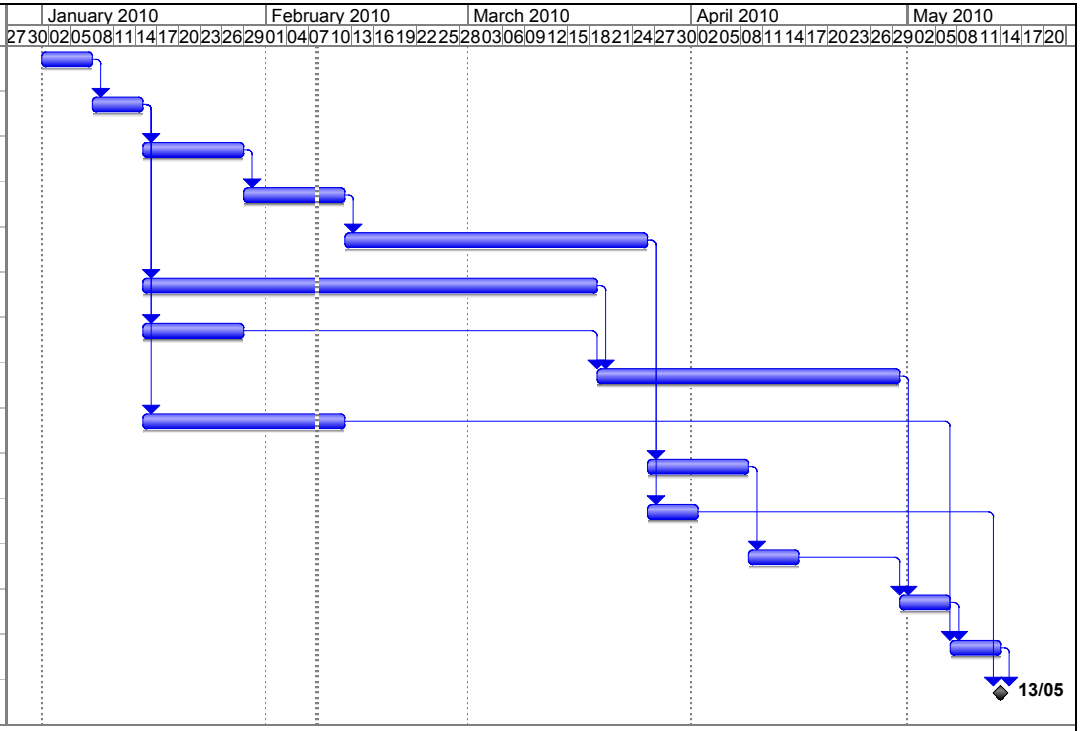

Project: Part II - 6
Date: Mon 08/02/10

Task	Milestone	External Tasks	
Split	Summary	External Milestone	
Progress	Project Summary	Deadline	
